


MNRE · NATIONAL GREEN HYDROGEN MISSION · 2026

A national registry for a process that did not yet exist

India had no digital certification process for green hydrogen, so the process was defined before anything was built. The registry is append-only, passed an external security audit, and has an advisory AI layer scoped for Phase 2.

ROLE Project Manager Process definition to production, and the Phase 2 AI scope	SCOPE 4 certificate types Append-only national registry under MNRE	SPAN Jan to mid-2026 Live since mid-2026	HEADLINE 48 of 51 closed Findings, before the external audit opened
---	--	--	---

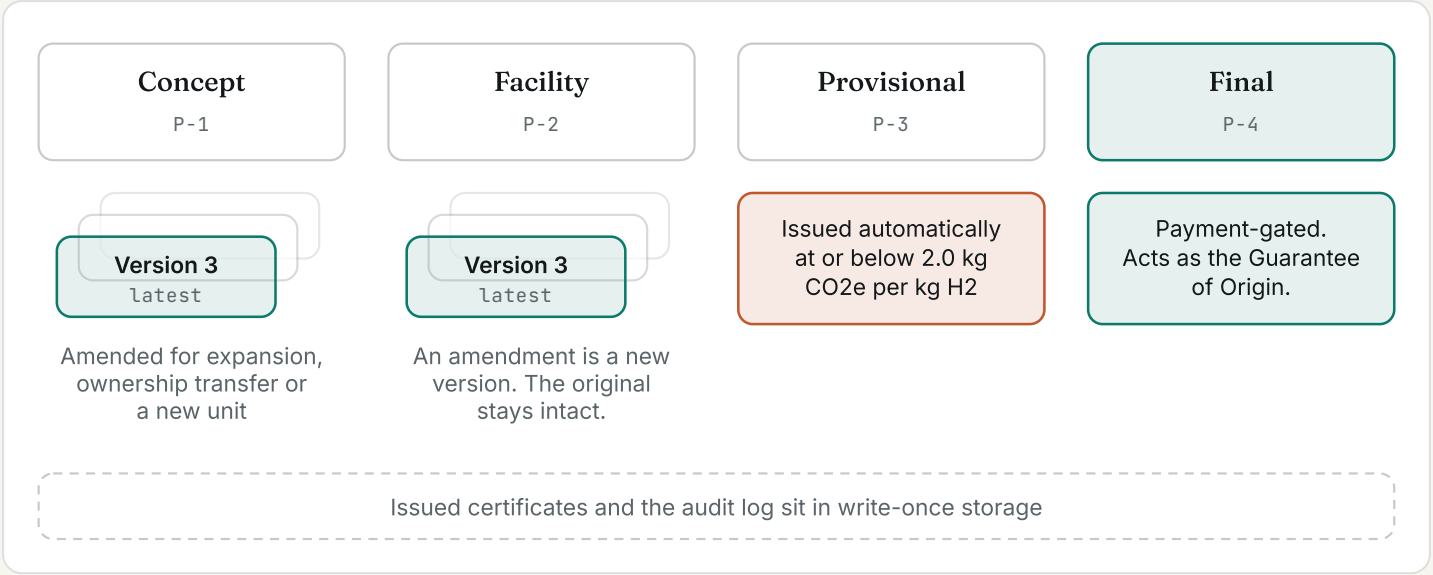

THE CONSTRAINT, AND THREE DECISIONS

- No existing certification process, so no benchmark to build against
- An external security audit stood between the build and production
- Validation rules that change through office memoranda, not releases

1. Append-only registry.

An amendment becomes a new record and the original stays intact.

COST Storage, harder read paths, an interface that must name the version.

2. Internal security review first.

The external audit met a platform already attacked.

COST Security effort pulled into a busy window.

3. AI held out of Phase 1.

Auditors learn the process before they judge an assistant.

COST A phase of efficiency delayed.

OUTCOME

48 / 51 findings closed before the external audit	Mid-2026 public launch
4 certificate types	66 fixes closed before UAT submission

AI advises. A named officer approves every consequential action.

Every generated claim cites the document supporting it.

Phase 2 AI: client approval received, procurement in progress. Expected outcomes are targets, not results.



Read the full case study
notrishabhjain.github.io/work/green-hydrogen-certification/

rishabh.jain@outlook.in
linkedin.com/in/notrishabhjain
 Delhi · open to relocation and remote
