
MNRE · NATIONAL GREEN HYDROGEN MISSION · 2026

A national registry for a process that did not yet exist

There was no process for certifying green hydrogen in India, so I started by defining one with the ministry. We then built the portal around it and passed an external security audit, and the Minister launched it on 1 July 2026.

ROLE	SCOPE	SPAN	HEADLINE
Project Manager	**4 certificate types**	**Jan to Jul 2026**	**8 certificates issued**
Process definition to production, and the Phase 2 AI scope	11 modules, a team of ten, under MNRE	Public launch on 1 July 2026	From 20+ applications; 8 producers, 3 ACV, 4 TC

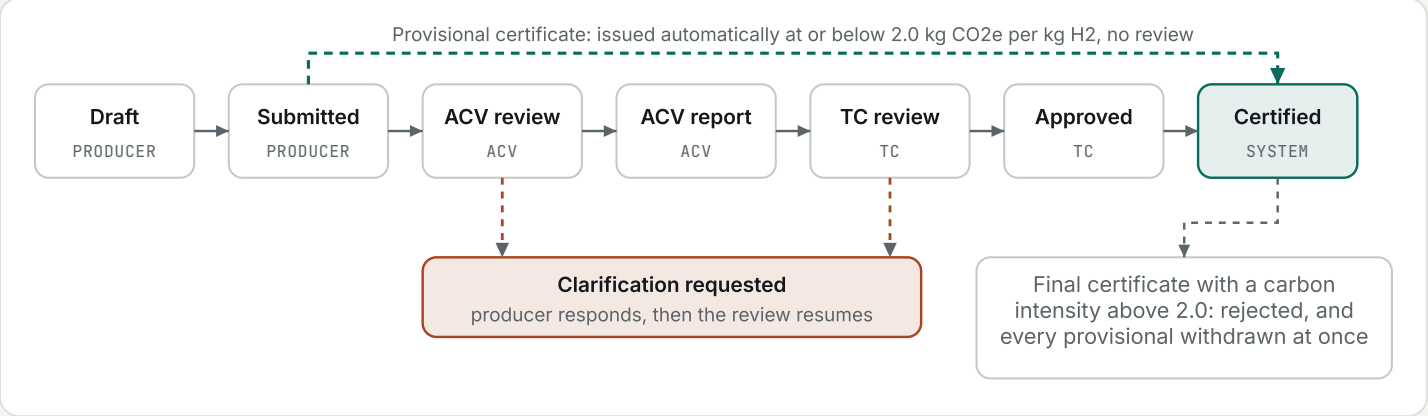

THE CONSTRAINT, AND THREE DECISIONS

- No existing certification process, so no benchmark to build against
- An external security audit stood between the build and production
- Validation rules that change through office memoranda, not releases

1. Append-only registry.
An amendment becomes a new record and the original stays intact.
COST Storage, harder read paths, an interface that must name the version.

2. Internal security review first.
The external audit met a platform already attacked.
COST Security effort pulled into a busy window.

3. AI held out of Phase 1.
Auditors learn the process before they judge an assistant.
COST A phase of efficiency delayed.

OUTCOME

8 certificates issued, from 20+ applications	**1 Jul** public launch, by the Minister
48 / 51 internal findings closed before the external audit	**3 days** for a change request that altered the workflow

> AI advises. A named officer approves every consequential action.

> Every generated claim cites the document supporting it.

Phase 2 AI: client approval received, procurement in progress. Expected outcomes are targets, not results.

Read the full case study
notrishabhjain.github.io/work/green-hydrogen-certification/

rishabh.jain@outlook.in
linkedin.com/in/notrishabhjain
Delhi · open to relocation and remote
